

Project Planning Phase
Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	30 June 2026
Roll Number	23A51A42B1
Project Name	Laptop Request Automation using ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority
Sprint-1	Service Catalog Setup	USN-1	As an employee, I can access the Laptop Request catalog item from the Service Catalog.	2	High
Sprint-1	Service Catalog Setup	USN-2	As an administrator, I can create the Laptop Request catalog item with required details.	2	High
Sprint-1	Catalog Variables	USN-3	As an employee, I can enter Purpose, Laptop Type, Manager, Business Justification, Required Date, and Confirmation.	3	High
Sprint-1	Workflow Automation	USN-4	As a system, I automatically trigger the workflow when a laptop request is submitted.	3	High
Sprint-1	Manager Approval	USN-5	As a manager, I can approve or reject the laptop request.	5	High

Sprint-2	Flow Designer	USN-6	As a system, I evaluate the manager's approval decision using Flow Logic.	3	Medium
Sprint-2	Catalog Task	USN-7	As a system, I automatically create a Catalog Task after approval.	5	High
Sprint-2	Email Notifications	USN-8	As a requester, I receive an email notification after approval.	2	Medium
Sprint-2	Email Notifications	USN-9	As the IT Support team, I receive an email when a Catalog Task is created.	2	Medium
Sprint-2	Request Tracking	USN-10	As an employee, I can track the status of my laptop request.	3	High
Sprint-2	Testing & Validation	USN-11	As an administrator, I can test the complete workflow and ensure successful execution.	5	High

Project Tracker , Velocity and Burndown Chart (4 Marks)

Project Tracker

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	15	7 Days	16 June 2026	22 June 2026	15	22 June 2026
Sprint-2	20	8 Days	23 June 2026	30 June 2026	20	30 June 2026

Velocity:

Formula: Velocity = Total Story Points Completed ÷ Number of Sprints

Calculation:

Total Story Points = 35

Number of Sprints = 2

Velocity = $35 \div 2$

Velocity = $17.5 \approx 18$ Story Points per Sprint

Average Velocity Per Day:

Formula: Average Velocity = Sprint Story Points ÷ Sprint Duration

Sprint-1:


$15 \div 7 = 2.14$ Story Points/Day

Sprint-2:

$20 \div 8 = 2.50$ Story Points/Day


Average : $(2.14 + 2.50) \div 2 = 2.32$ Story Points/Day

Burndown Chart

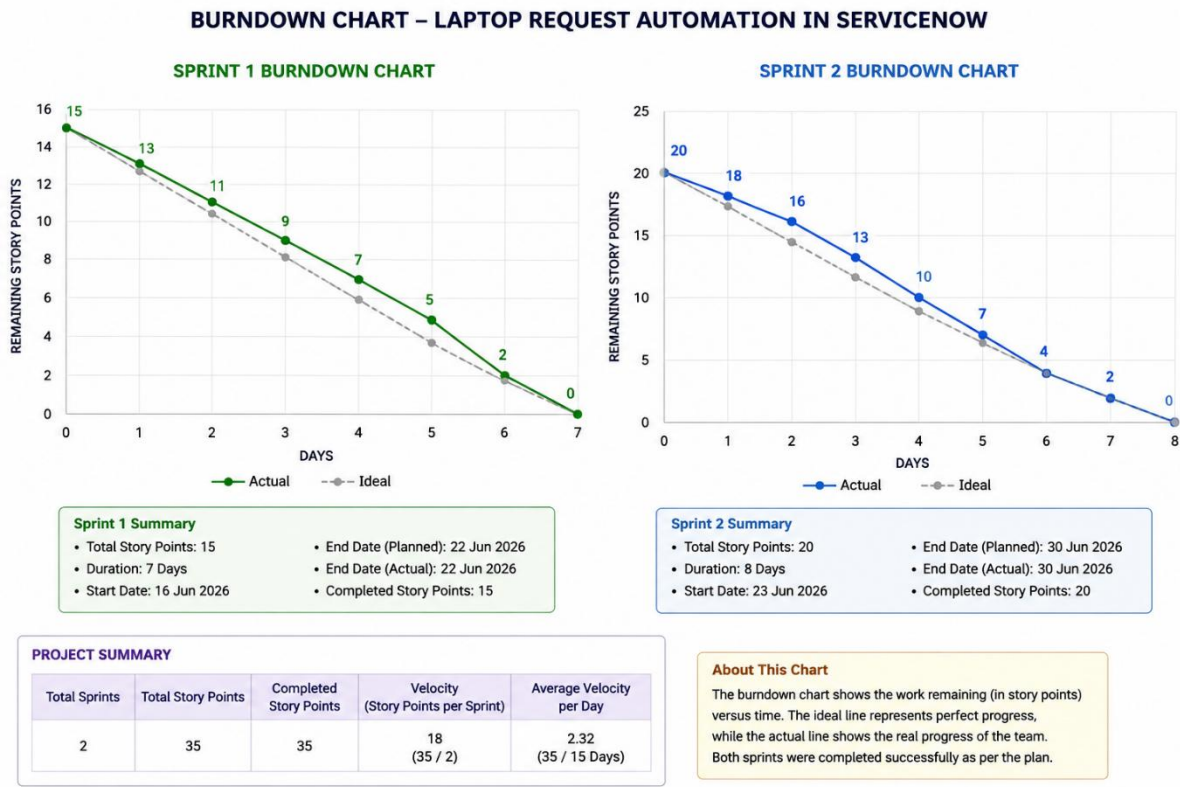

PROJECT PLANNING

The project was planned in a structured manner to automate the network request management process in ServiceNow. The planning includes requirement analysis, design, development, testing and deployment.



PROJECT LOGIC (WORKFLOW)

The system follows an automated workflow from request submission to closure with approvals, notifications and status updates.

